

Implement Client Script & UI Policy (Incident)

Phase 4: Project Planning Phase

Item	Details
Project Name	Implement Client Script & UI Policy (Incident)
Platform	ServiceNow
Target Table	Incident [incident]
Team ID	SWTID-2026-7176_____
Team Size	5 members
Total Project Time	3 hours
Sprints	3 sprints of 1 hour each
Total Story Points	25

1. Introduction

The Project Planning Phase turns the requirements and design from the earlier phases into a schedule the team can follow. It lists the work as a product backlog, groups it into sprints, estimates each item in story points, and assigns every item to team members. This project is a short micro project, so the plan is built around a total of 3 hours and a team of 5.

The plan covers the five configuration tasks from the project guide (UI Policy, UI Policy Action for Urgency, onChange, onSubmit and onCellEdit scripts), the testing activities, and the final documentation and demonstration.

2. Team and Responsibilities

Replace the placeholders with the actual names of the team members.

Member	Name	Main Responsibility
Team Member 1	Mohamed Ayman	UI Policy creation, onSubmit Client Script, reverse condition testing
Team Member 2	Noor Mohamed	UI Policy Action for Assignment group, onCellEdit Client Script (with Member 5), reverse condition testing
Team Member 3	Dhamotharan	UI Policy Action for Urgency, mandatory and successful-save testing, list and form update testing
Team Member 4	Uwais Ahamed	onChange Client Script, mandatory and successful-save testing, list and form update testing
Team Member 5	Mohamed Milkan	onChange Client Script (with Member 4), onCellEdit support, documentation and demonstration

3. Product Backlog, Sprint Schedule and Estimation

Each user story is estimated in story points, where 1 is a very small task and 3 is the largest task in this project. Priority is High for the controls that enforce the main business rules and Medium for supporting checks.

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Members
1	Field Control (UI Policy)	USN-1	Create the High Impact Control UI Policy on Incident with condition Impact is 1 - High, Reverse if false and On load	3	High	Member 1
1	Field Control (UI Policy)	USN-2	Add the UI Policy Action on Assignment group with Mandatory set to True	2	High	Member 2
1	Field Control (UI Policy)	USN-3	Add the UI Policy Action on Urgency with Read-only set to True and Visible left alone	2	High	Member 3
1	Automation (Client Script)	USN-4	Create the onChange script on Impact that sets Urgency to High and shows a message	3	High	Members 4, 5
2	Validation (Client Script)	USN-5	Create the onSubmit script that blocks the save when Impact is High and Assigned to is empty	3	High	Member 1
2	List Control (Client Script)	USN-6	Create the onCellEdit script on State that shows an alert and cancels the list edit	2	Medium	Members 2, 5
2	Testing	USN-7	Test mandatory enforcement (save blocked with error) and successful save with Assigned to filled	3	High	Members 3, 4
3	Testing	USN-8	Test the reverse condition by changing Impact from High to Medium	2	Medium	Members 1, 2
3	Testing	USN-9	Test list edit blocking and the form-based State update	2	Medium	Members 3, 4
3	Final Delivery	USN-10	Compile the project documentation and prepare the demonstration with screenshots	3	Medium	Member 5 (all review)

Total: 10 user stories and 25 story points.

4. Sprint Planning

4.1 Sprint Summary

Sprint	Goal	Total Story Points	Duration	Story Points Completed	Sprint End
Sprint 1	Build the UI Policy, both UI Policy Actions and the onChange script	10	1 hour	10	End of Hour 1

Sprint	Goal	Total Story Points	Duration	Story Points Completed	Sprint End
Sprint 2	Build the onSubmit and onCellEdit scripts and test save validation	8	1 hour	8	End of Hour 2
Sprint 3	Complete the remaining tests and finish the documentation and demo	7	1 hour	7	End of Hour 3
Total		25	3 hours	25	

Sprint start and end dates are not filled in because the project ran as one continuous 3-hour session. Add the dates in the header of this document if your submission needs them.

4.2 Hour-by-Hour Plan

Time	Sprint	Focus	Outcome
Hour 1	Sprint 1	Log in with admin access, create the High Impact Control UI Policy and its two UI Policy Actions, then add the onChange script	Impact High makes Assignment group mandatory and Urgency read-only and set to High
Hour 2	Sprint 2	Add the onSubmit and onCellEdit scripts, then test the blocked save and the successful save	Save is blocked without Assigned to; list edits of State are refused
Hour 3	Sprint 3	Test the reverse condition, list edit blocking and the form update, then compile the documentation and demo	All behaviours verified and the deliverables are ready

5. Velocity and Burndown


5.1 Velocity

The team completed 25 story points across 3 sprints of 1 hour each.

- **Average velocity** = 25 story points ÷ 3 sprints = about 8.3 story points per sprint (per hour).
- **Per member** = 25 story points ÷ 5 members = 5 story points per member on average.
- **Sprint velocity** = 10, 8 and 7 story points in Sprints 1, 2 and 3.

5.2 Burndown

Point in Time	Story Points Remaining	Story Points Completed
Start of project	25	0
End of Sprint 1 (Hour 1)	15	10
End of Sprint 2 (Hour 2)	7	18
End of Sprint 3 (Hour 3)	0	25

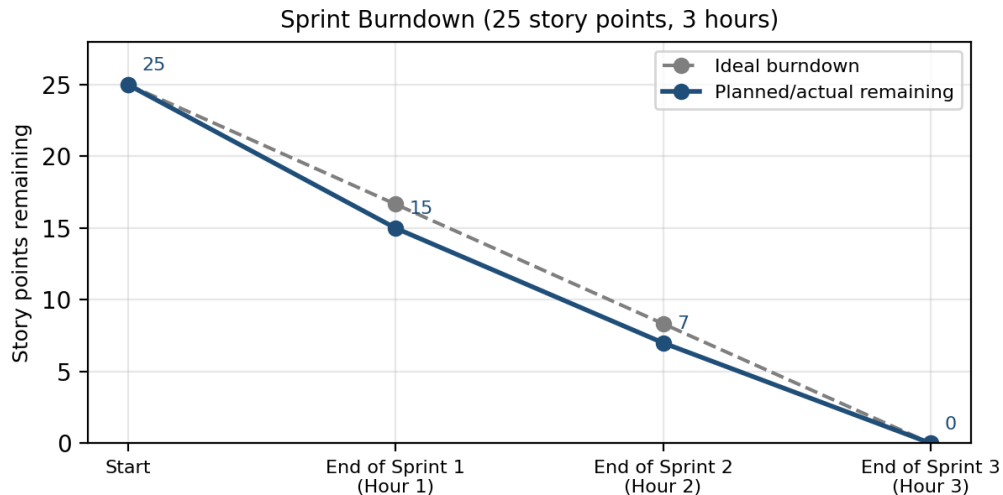

6. Risks and Mitigation

Risk	Impact	Mitigation
Project guide mixes Assignment group and Assigned to (the UI Policy makes Assignment group mandatory, the onSubmit script and tests use Assigned to)	Testers may expect the wrong field to be enforced	State both rules clearly in the test cases: Assignment group by the UI Policy, Assigned to by the onSubmit script
The onChange script in the text uses addInfoMessage, while the screenshot shows showFieldMsg	Different messages appear depending on which version is used	Use one version, and keep the same message in the test and the documentation
The onCellEdit script in the text calls callback(false), while the screenshot calls callback(false, oldValues)	List edit may not revert cleanly in some cases	Use the screenshot version and confirm State stays unchanged in USN-9
Client-side controls do not cover API, import or server-side updates	Incomplete data can still arrive through those channels	Record a server-side Business Rule or Data Policy as a future enhancement
Only 3 hours are available	Testing or documentation may be rushed	Keep the sprints small and run tests in parallel by pairing members

7. Conclusion

The plan splits the project into 10 user stories worth 25 story points and delivers them in three 1-hour sprints with a team of five. Sprint 1 builds the form controls, Sprint 2 adds validation and list control, and Sprint 3 completes testing and documentation. The velocity of about 8.3 story points per hour and the burndown to zero show that the scope fits within the 3 hours consumed. The next phase covers development and execution.
